

June 9, 2015

OVERVIEW

- Milestones
- Budget Update
- Current Construction Highlights
- Equipment Update


- Naming update [North]
- Pond Area Development
- Status of Dead Trees
- Environmental Assessment [North]

MILESTONES

"Desert Sage Youth Wellness Center"

- Contract Award03 November 2014
- Start of Construction......03 December 2014
- Projected Completion......18 December 2015
- Original Construction Contract: \$12.82 Million
- Current Construction Contract: \$12.94 Million
 - Includes 10 Change Orders/Contract Mods
- Facility Size: 35,455 square feet

BUDGET UPDATE - Construction

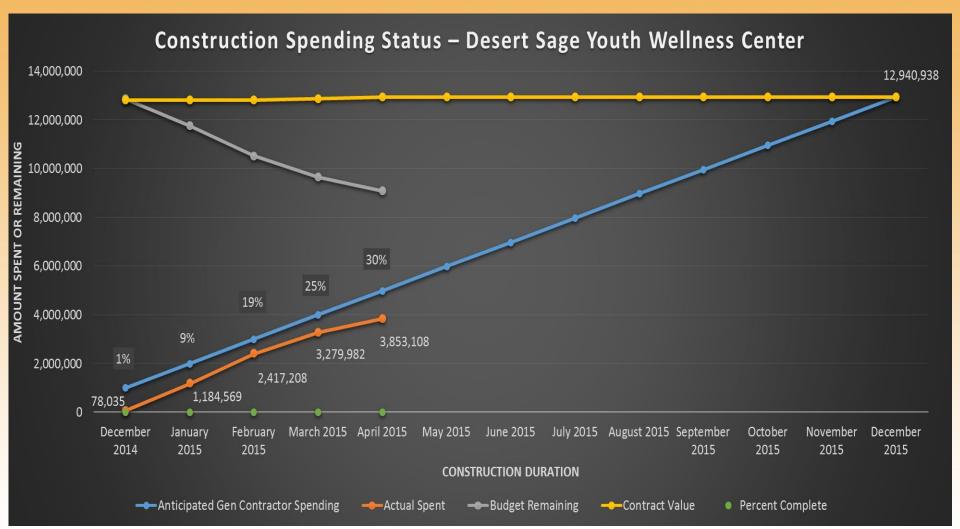

BUDGET UPDATE -- Significant Contract Mods

- Well Drilling \$65k, Construction
- Cultural Building Sprinklers \$30k, Construction
- Equipment Coordinator \$50k estimate only, A&E

CONSTRUCTION HIGHLIGHTS

- Structural steel Complete for all buildings
- Glulam Beams Complete for all buildings
- Ceilings Joists Complete for all buildings
- Insulated Concrete Filled (ICF) Walls in progress



Example - Insulated concrete filled (ICF) wall



Resident Building (A) – Placing concrete in ICF wall



Resident Building (A) – Placing concrete in ICF wall



Resident Building (A)



Cultural Building (E) – Structural Steel, Glulam Beams, Rebar



Admin/Therapy Building (C) – Glulam Beams, Joists, & ICF Walls



Admin/Therapy Building (C) – Prep for ICF Wall



Gymnasium (B) – Pumping concrete to ICF Wall

Construction Milestones - Upcoming

- Water Well Well pump test and installation
- IT Equipment Needed for Communication & Data Systems Commissioning


Naming Update -- North <u>"SACRED OAKS HEALING CENTER"</u>

- Request for Name suggestions
- Approved by CATAC
- Approval of CATAC Minutes
- Forward to IHS DFO

February 2015 March 2015 June 2015 June 2015

Development of the Pond area

- Pond is not part of programmed elements of YRTC in Program Justification Document (2004)
- No Federal funding for Pond area
- Tribal Leaders have identified Pond area as great benefit to the site
- IHS HQ has approved CAO working with Tribes

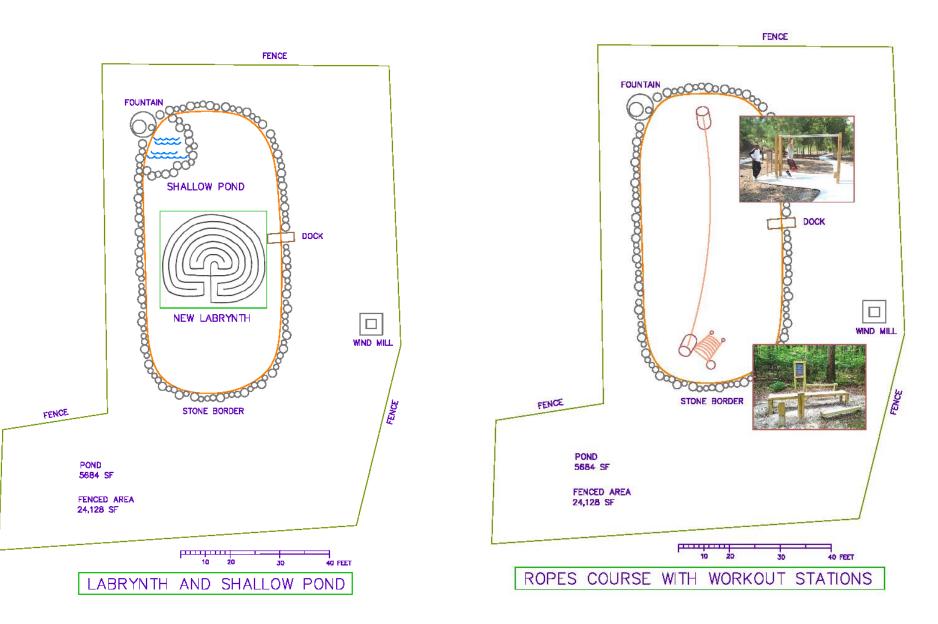


Status of Dead Trees

- 48 trees have been killed by Bark Beetle
- Arborist Report stated that the infestation is very wide spread
- All dead trees have been marked for removal
- Contract for removal is an add to general contract

Environmental Assessment

- Required by National Environmental Protection Act
- Division of Engineering Services, Dallas is contracting
- Evaluate impact on traffic, sound, utilities, farmland and endangered or threatened species
- Requires 60 90 days with local input
- Can run concurrent with design

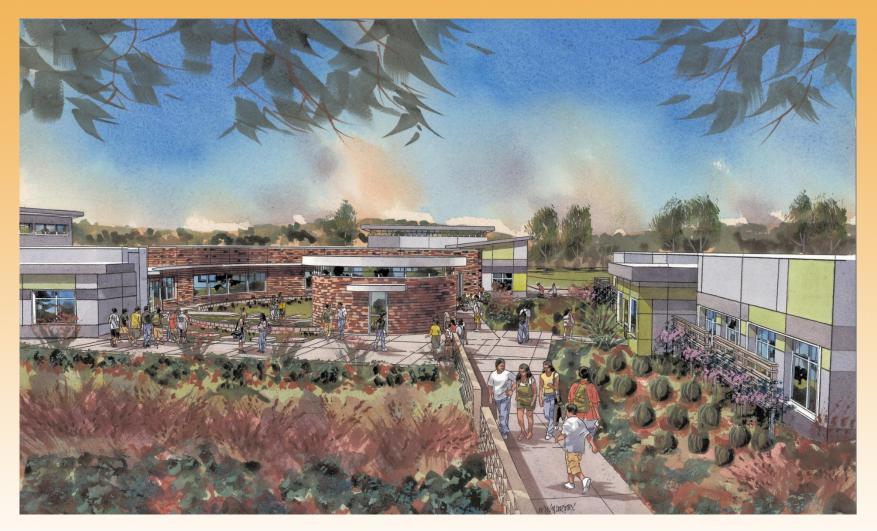

Artist's Rendering of Completed YRTC
