

CAO INDIAN HEALTH SERVICE DESERT SAGE YOUTH WELLNESS CENTER CONSTRUCTION UPDATES

PRESENTED AT 2018 ANNUAL TRIBAL CONSULTATION

MARCH 21, 2018




FACILITY UPDATES

- Completed Project
 - Disposal Field Expansion
- Ongoing Project
 - Backup Power
- Best Road Update


COMPLETED PROJECT

- Disposal Field Expansion
 - Project Completed on December 19, 2017
 - Added 2 disposal fields @ 3,120 SF each.
 - Provides operational flexibility to alternate fields

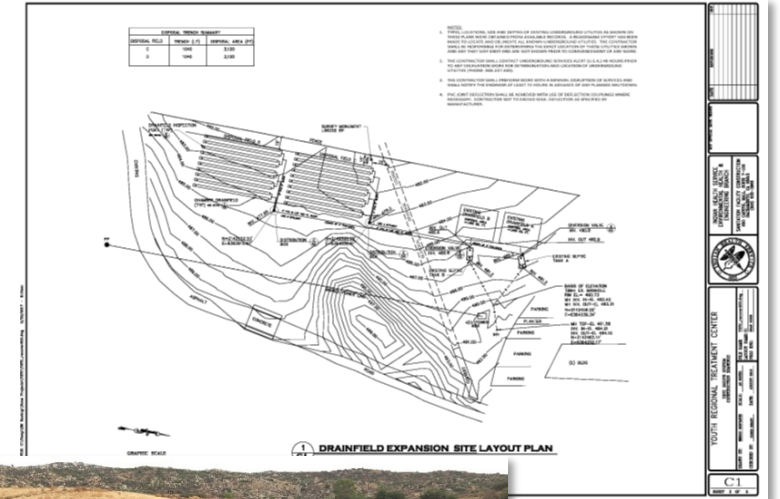

ONGOING PROJECT

- Backup Power – Diesel Generator
 - Design Build Team
 - RFE Engineering/Trinity Built
- Project Schedule
 - Design
 - Completed - February 2, 2018
 - Construction
 - Start – February 12, 2018
 - Planned Completion – March 23, 2018

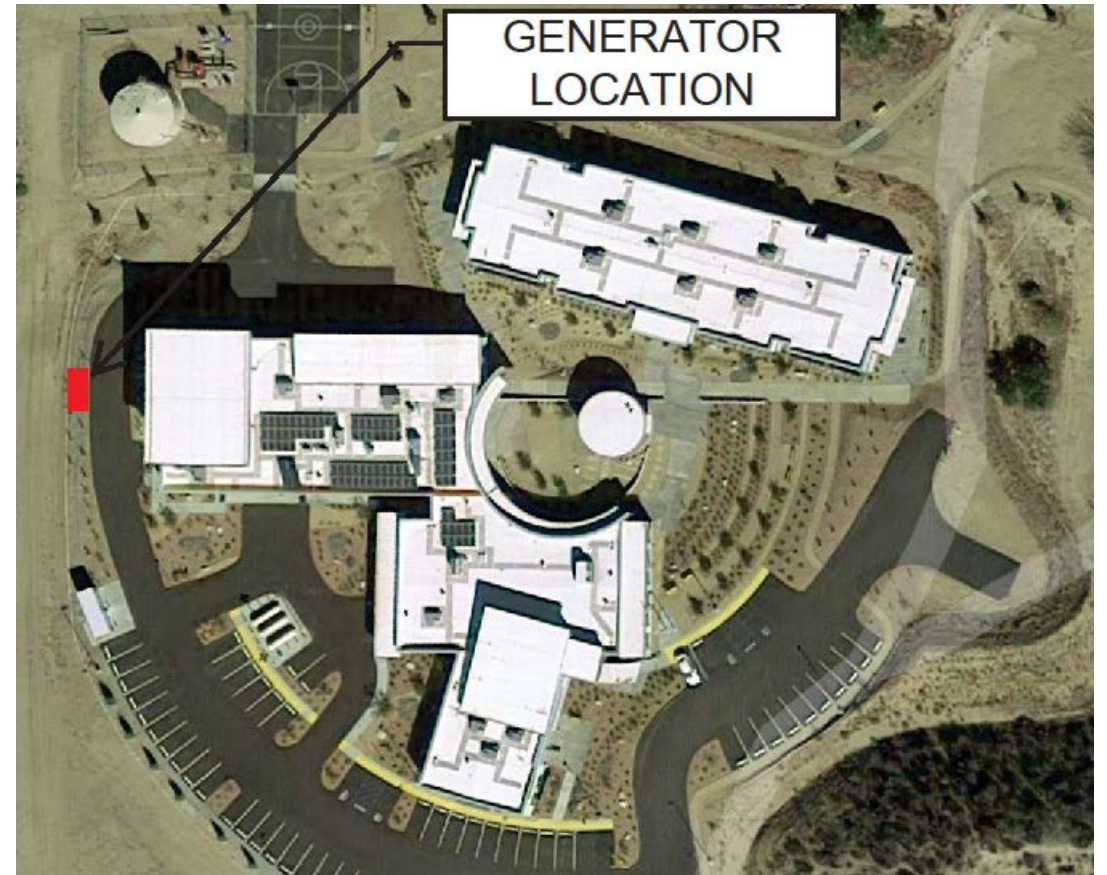

ONGOING PROJECT




BEST ROAD UPDATE

- Current Update
 - Riverside County identifies Best Road as a private road.
 - Requires dedicated right of way for major road work.
 - Ongoing minor road maintenance
 - scheduled bi-monthly.
 - Emergency repairs as needed.



BEST ROAD

- Next Steps
 - Met with Riverside County on 12/19/2017 to discuss access alternatives for Best Road
 - Riverside County has no exceptions to constructing a road within the existing easement.
 - Preliminary engineering report to develop alternatives for Best Road.

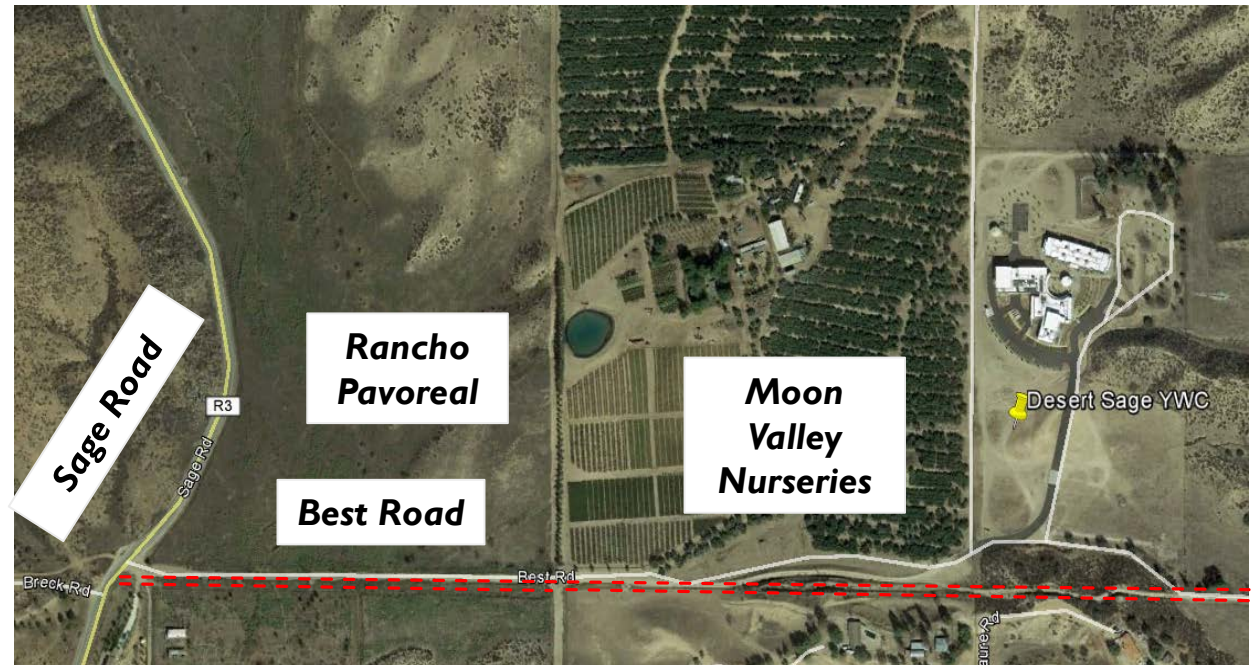

CONTACT INFORMATION

CDR Frank Chua, PE

francis.chua@ihs.gov

916-930-3981, ext. 347
