



Santa Fe Service Unit

*Electronic Health Record
(EHR)*

*Implementation
2005-2006*

*Presented By:
Lori Moore Pharm D., CAC
September 15, 2005*

SFSU

Santa Fe Indian Hospital

Santa Clara Health Center

Santo Domingo Health Center

San Felipe Health Center

Cochiti Health Center

EHR Multidisciplinary Work Group

■ August 2004

- Pharmacist (2)
- Lab Supervisor (1)
- Radiology Supervisor (1)
- Medical Records/Data Entry Supervisor (1)
- IT Supervisor (1)
- Clinical Staff Member (1)
- Patient Registration & Billing Staff (2)
- Off Site Clinic Staff [SCHC (1), SD/CO/SF (1)]

EHR Allocated Funds

- In 2004 SFSU was allocated \$120,000.00 to implement EHR
 - Cabling Project
 - \$16,500.00
 - 2 - PowerEdge 285 Servers, tape backup, & UPS
 - \$32,000.00
 - 11 - 24 Port Switches with equipment
 - \$34,000.00
 - 8 - Dell Latitude laptops with Office professional 2003 software
 - \$17,000.00
 - 12 - Thin Clients including MS Office 2003, MetaFrame, & Citrix
 - \$19,000.00

Information Technology

“FAT FARM”


Thin Client



Fat Client



EHR Implementation

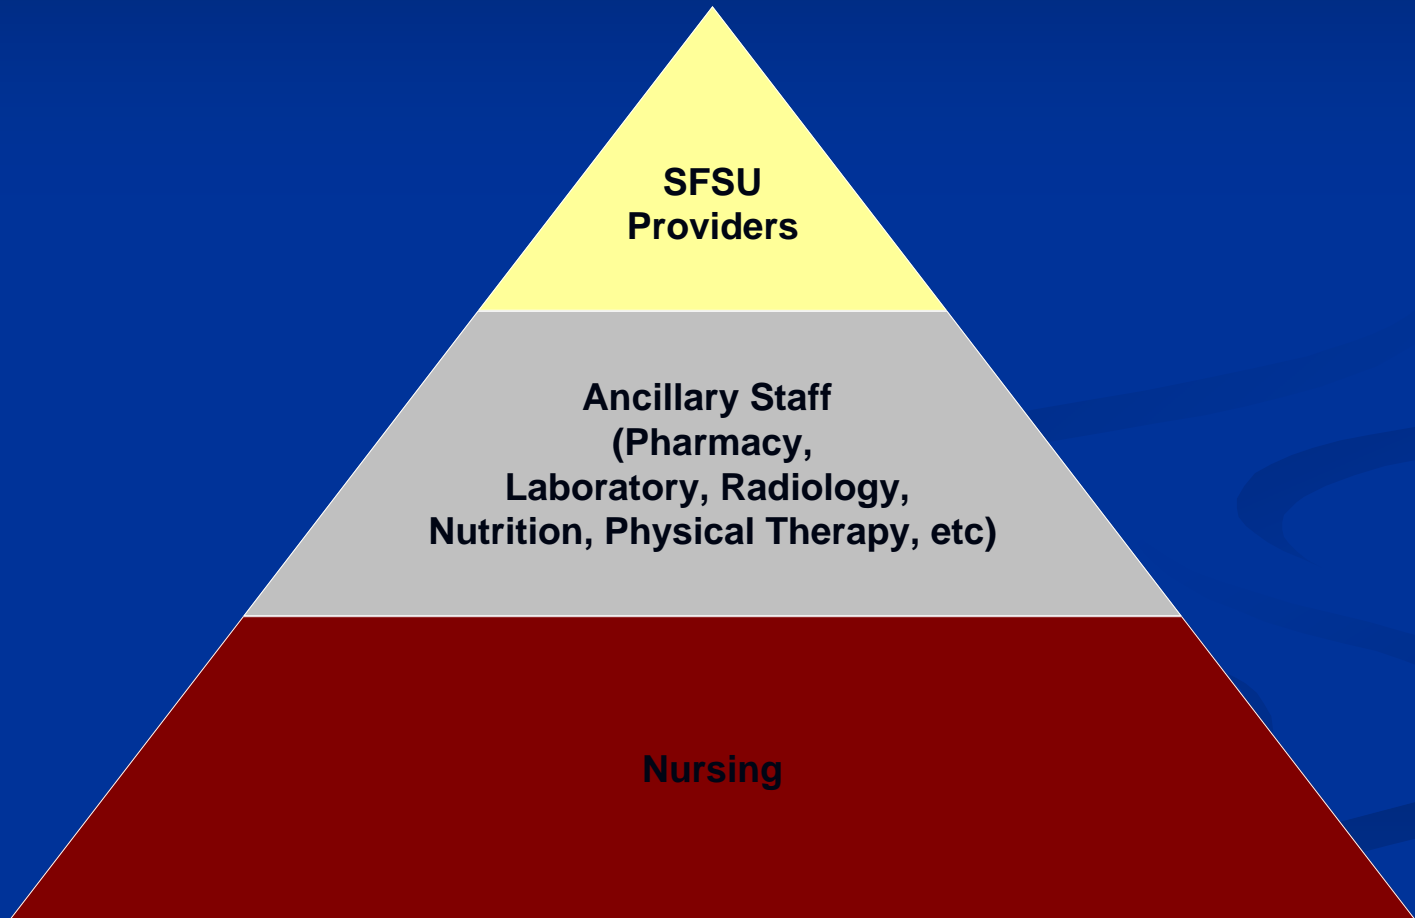

SFSU EHR Implementation Plan

			10/7-10/10/05	10/10 - 11/21/05	11/21-1/2/06	1/2 - 2/13/06	2/13 - 3/27/06	3/27 - 5/8/06	5/8 - 6/19/06	6/19 - 7/31/06	7/31/06 - 9/11/06	9/11 - 10/23/06	
6 WK IMPLEMENTATION													
PHASE ONE	TRIAGE TAB	Nursing	SET UP										
	WELLNESS TAB	Nursing		10/10 - 11/18/05									
	LABORATORY/RADIOLOGY TAB	Nursing, Providers, Pharmacist											
PHASE TWO	ANTICOAGULATION	Matt R., Chi, Gina, Nekia, Lori		6 WK IMPLEMENTATION									
	HEPATITIS C /SMOKING CESS.	Nekia, Gina, Lori, Matt E.		11/21-12/30/06									
	GRANT CONTINUITY CLINIC	Grant											
PHASE THREE	NEPHROLOGY	Nava		6 WK IMPLEMENTATION									
	DIABETES CLINIC	Walker, Smoker, Gregory, Toomey, Lujan		1/2 - 2/10/06									
	DIABETES CLINIC	Walker, Smoker, Gregory, Toomey, Lujan											
PHASE FOUR	EYE CLINIC	Stadick, Cespon		6 WK IMPLEMENTATION									
	NUTRITION	Butler		2/13 - 3/24/06									
	PHYSICAL THERAPY	DOUGAN											
PHASE FIVE	NOTES	Behavioral Health, Well Child, Gynecology, Pediatrics, Prenatal, Surgery, & Dental	6 WEEK IMPLEMENTATION										
			3/27 - 5/5/06										
PHASE SIX	PROBLEM LIST PURPOSE OF VISIT (POV) SERVICES TAB	Behavioral Health, Well Child, Gynecology, Pediatrics, Prenatal, Surgery, & Dental	6 WK IMPLEMENTATION										
			5/8 - 6/16/06										
PHASE SEVEN	MEDICATION TAB	Behavioral Health, Well Child, Gynecology, Pediatrics, Prenatal, Surgery, & Dental	6 WK IMPLEMENTATION										
			6/19 - 7/28/06										
PHASE EIGHT	CONSULTS	Behavioral Health, Well Child, Gynecology, Pediatrics, Prenatal, Surgery, & Dental	6 WK IMPLEMENTATION										
			7/31 - 9/8/06										

EHR Implementation Plan Summary

- Primary goal is to CONTINUE providing high quality care to the SFSU patients
- EHR Implementation will be a Slow process
 - One year to completely implement
 - *Eight phases - each a minimum of six weeks long*
 - Minimize starting all providers at once due increased patient visits during the winter months
 - *Majority of providers will begin training in the spring of 2006*

EHR Implementation Plan Summary

- Hands on training
- Provide a solid foundation of trained staff before training providers
 - Includes nurses, pharmacist, lab staff, radiology staff, etc.

Future Needs

- Six additional data ports in Ext A/B & UC
- Replace current Windows Operation System (OS) 98's with newer OS
- Equipment
 - *Thin Clients*
 - *Fat Clients*

Future Needs

■ Staff

- *Information Technology*
- *Pharmacist/Pharmacy Techs*
- *Medical Records Staff*
- *Data Entry*

■ Equipment for Field Clinics

QUESTIONS

